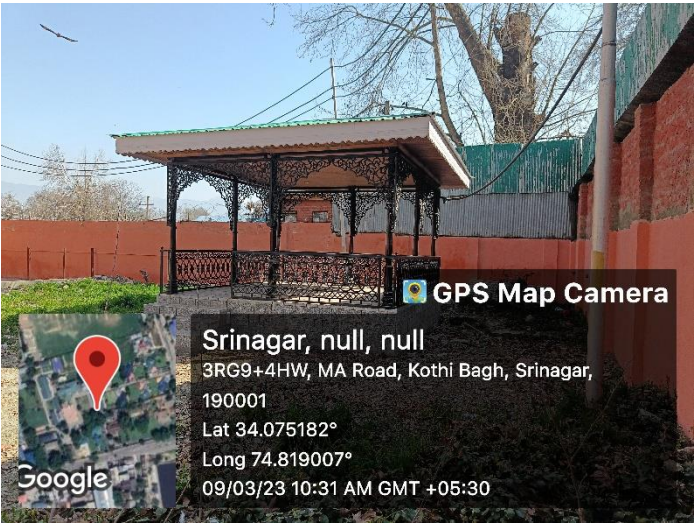
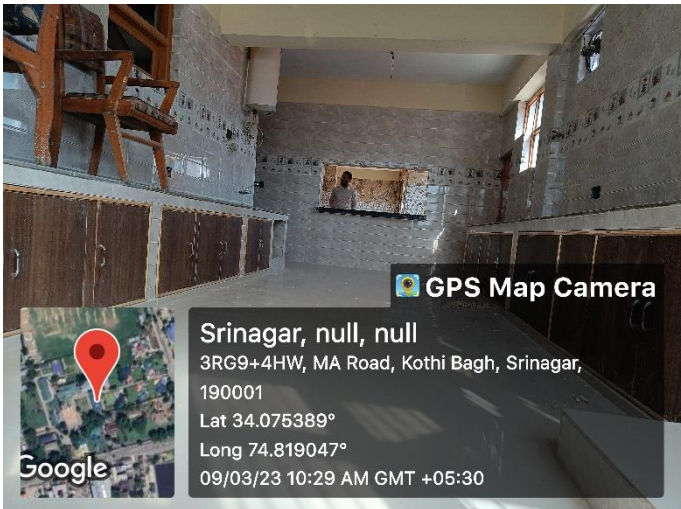


Geo-tagged Photograph (JPG Format) with details

	Sr. No (as per list)	02
	Name of the Work	Construction of Gazebo in various location at IMPARD Srinagar
	Department/Organisation	J&K IMPARD
	District	Srinagar
	Block	Srinagar
	Location Type (U/R)	M.A Road Srinagar
	Location of Work	J&K IMPARD M.A Road Srinagar
	Source of funding (Regular/Loan/CSS/PMDP/other specify)	Regular
	Executing Agency	R&B Construction Division, IInd, Srinagar
	Date of commencement (MM/YY)	August, 2022
	Date of completion (MM/YY)	Work completed
	AA/Approved Cost (Rs in Lakh)	Rs. 12.77 Lacs
	Completion cost (Rs in Lakh)	Rs. 12.77 Lacs
No. of Beneficiaries		

Geo-tagged Photograph (JPG Format) with details

	Sr. No (as per list)	01
	Name of the Work	Providing/laying of Floor/Wall Tiles in Canteen/Kitchen located in Administrative block IMPARD Srinagar.
	Department/Organisation	J&K IMPARD
	District	Srinagar
	Block	Srinagar
	Location Type (U/R)	M.A Road Srinagar
	Location of Work	J&K IMPARD M.A Road Srinagar
	Source of funding (Regular/Loan/CSS/PMDP/other specify)	Regular
	Executing Agency	R&B Construction Division, IInd, Srinagar
	Date of commencement (MM/YY)	October, 2022
	Date of completion (MM/YY)	Work completed
	AA/Approved Cost (Rs in Lakh)	Rs. 06.91 Lacs
	Completion cost (Rs in Lakh)	Rs. 05.98 Lacs
	No. of Beneficiaries	
